

Alamance County Oversight Meeting

Project Updates

February 29, 2024

Transforming lives through excellence
in teaching, learning, and service.



Public Safety Training Center

- Site clearing continues
- Rough grade for classroom building pad and parking lot complete
- Footing excavation and underground utilities to begin in next 30 days
- Grading for firing range building pad to begin in next 30 days



Administration/Classroom Building location February 2024



Public Safety Training Center

- Some bad weather days in February, but project remains on schedule
- Substantial completion:

*Admin Classroom Building
March/April 2025*

*Firing Range
July 2025*



Overall Training Center Site February 2024



Main, Powell, Gee Project Construction Progress



- Asbestos tile abatement ongoing
- Electrical/plumbing rough-in in progress
- Framing in progress
- Insulation and drywall underway
- Phase One on schedule for completion mid-May 2024

- Nursing Expansion
- Library renovation
- Skills / Tutoring Center

Skills / Tutoring Center– Main Building February 2024

Pay-GO CIP Projects

Gee Building Chiller Project Complete



Wayfinding Master Plan


- Master plan complete for public bid process – new exterior signage
- New signage to be funded through State SCIF funding



Exterior Signage Renderings



QUESTIONS ???

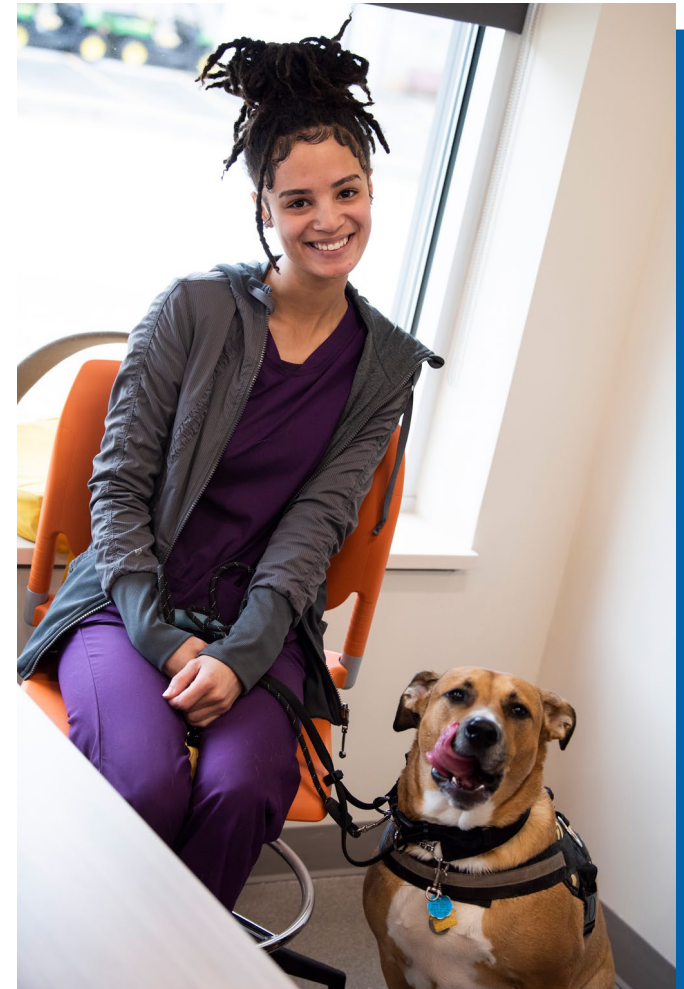

Animal Care Student. January 2022.

