

Alamance County Oversight Committee Meeting

PROJECT UPDATES

DECEMBER 8, 2022



www.alamancecc.edu

Biotechnology Center of Excellence & Parking Project



Biotechnology Center of Excellence & Parking Project



Second floor lab



First floor double classroom

Biotechnology Center of Excellence & Parking Project




Third floor wood slat ceiling



Main stairway from lobby

Biotechnology Center of Excellence & Parking Project

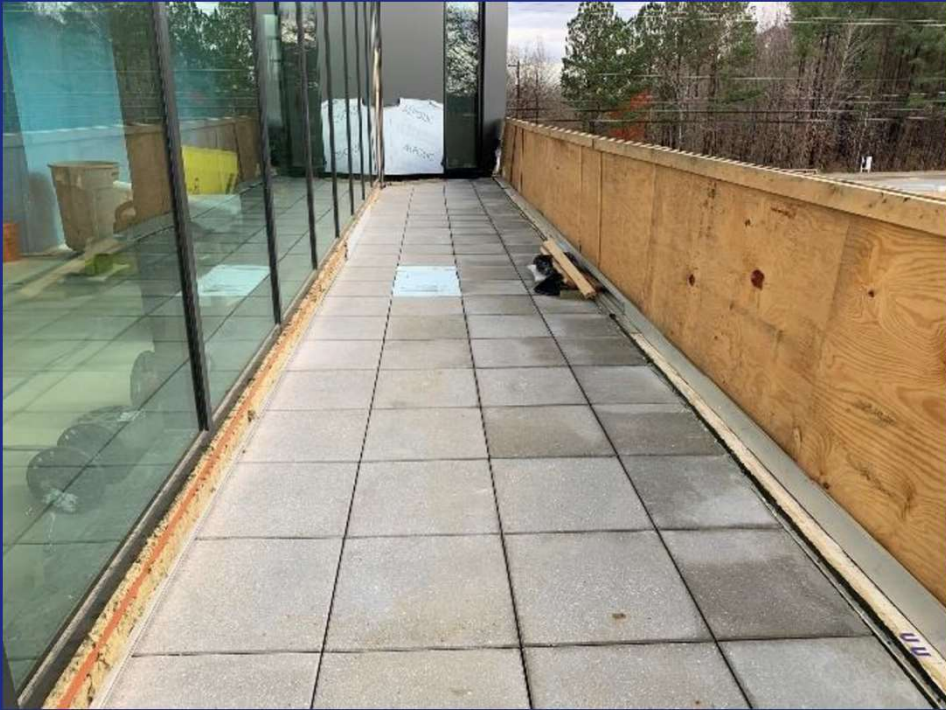

Second floor balcony space



Install of sidewalks at southern end

Biotechnology Center of Excellence & Parking Project



Grading of new remote parking lot

Biotechnology Center of Excellence & Parking Project

- Project 88% complete
- Project is on schedule and on budget
- Contract completion date is January 11, 2023
- Equipment and furniture installation begins mid January 2023

Student Services Center



Student Services Center



Main Entrance Lobby



Monumental stairway to lower level

Student Services Center



Lower level multipurpose/flex space



Multipurpose/flex space and stairs to main level

Student Services Center

- Project is 95% complete
- Project is on schedule and on budget
- Contract completion date is December 16, 2022
- Furniture and equipment installation begins January 9th with staff move-in end of January

Main, Powell & Gee Buildings – Classroom, Lab, Offices, Library Renovation/Nursing Expansion/Childcare Updates

- November cost estimate includes 8% in escalation by waiting to bid project with the PSTC in July.
- Avoidance of \$114,064 in escalation by bidding in mid-May and separating bond sale from the PSTC project timeline.



PUBLIC SAFETY TRAINING CENTER

