



# Alamance County Facilities update

Week ending February 17, 2023


# HVAC Replacement at HSC

**Began:** February, 2022

**Anticipated Completion:**  
~~February 2023~~ March 2023



# Emergency Services Center

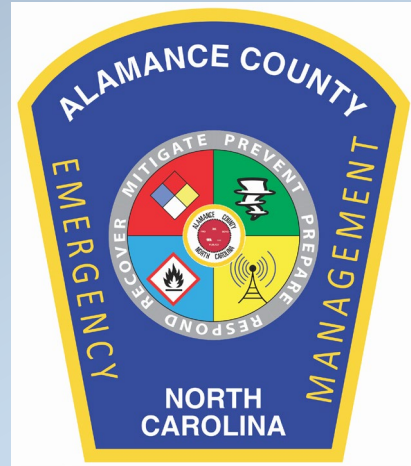

**Began:** February 2022  
**Anticipated Completion:**  
Spring 2025

- Moving forward with the purchase of the building 780 Plantation Drive. Closing should occur mid-April.
- Center will house Central Communications, Emergency Management, Fire Marshal's Office, and EMS Administration



# Board of Elections Building

**Began:** February 2022

**Anticipated Completion:**  
August, 2023

- Demolition started, will take approximately 2 weeks.



# Additional Projects

## **Detention Center Wall and Floor Cracks:**

Contractor waiting on subs to get in to finish project.

## **Court Administration Building and JB Allen renovation:**

County continues to review funding options.

## **EMS Substation in Mebane:**

Location has been identified. Site has been evaluated. Next step is land purchase.

# Additional Projects

## **Jail Hot Water Project**

Replacing 7 existing Rinnai water heaters with 2 Hot Water Boilers

## **Roof Replacement @ Ag Extension/Soil and Water Building**

Reviewing Contracts

## **Community Corrections Building**

HVAC Replacement--Complete
